FieldOps

Staffing & Operations Management

A working app for managers coordinating teams across different locations

Portfolio demonstration with simulated data

The operating problem

Enough workers on the schedule can still mean a missed client deadline

340

Accepted recordings required

320

Projected before intervention

In the retail scenario, quality review limits delivery. Additional collectors alone leave the forecast unchanged.


Fictional client scenario. Four-hour planning window. Delivery counts accepted work.

The manager’s operating view

60 workers
3 client projects

The overview connects current staffing with accepted output and delivery risk.

Managers open an at-risk project to inspect the constraint.

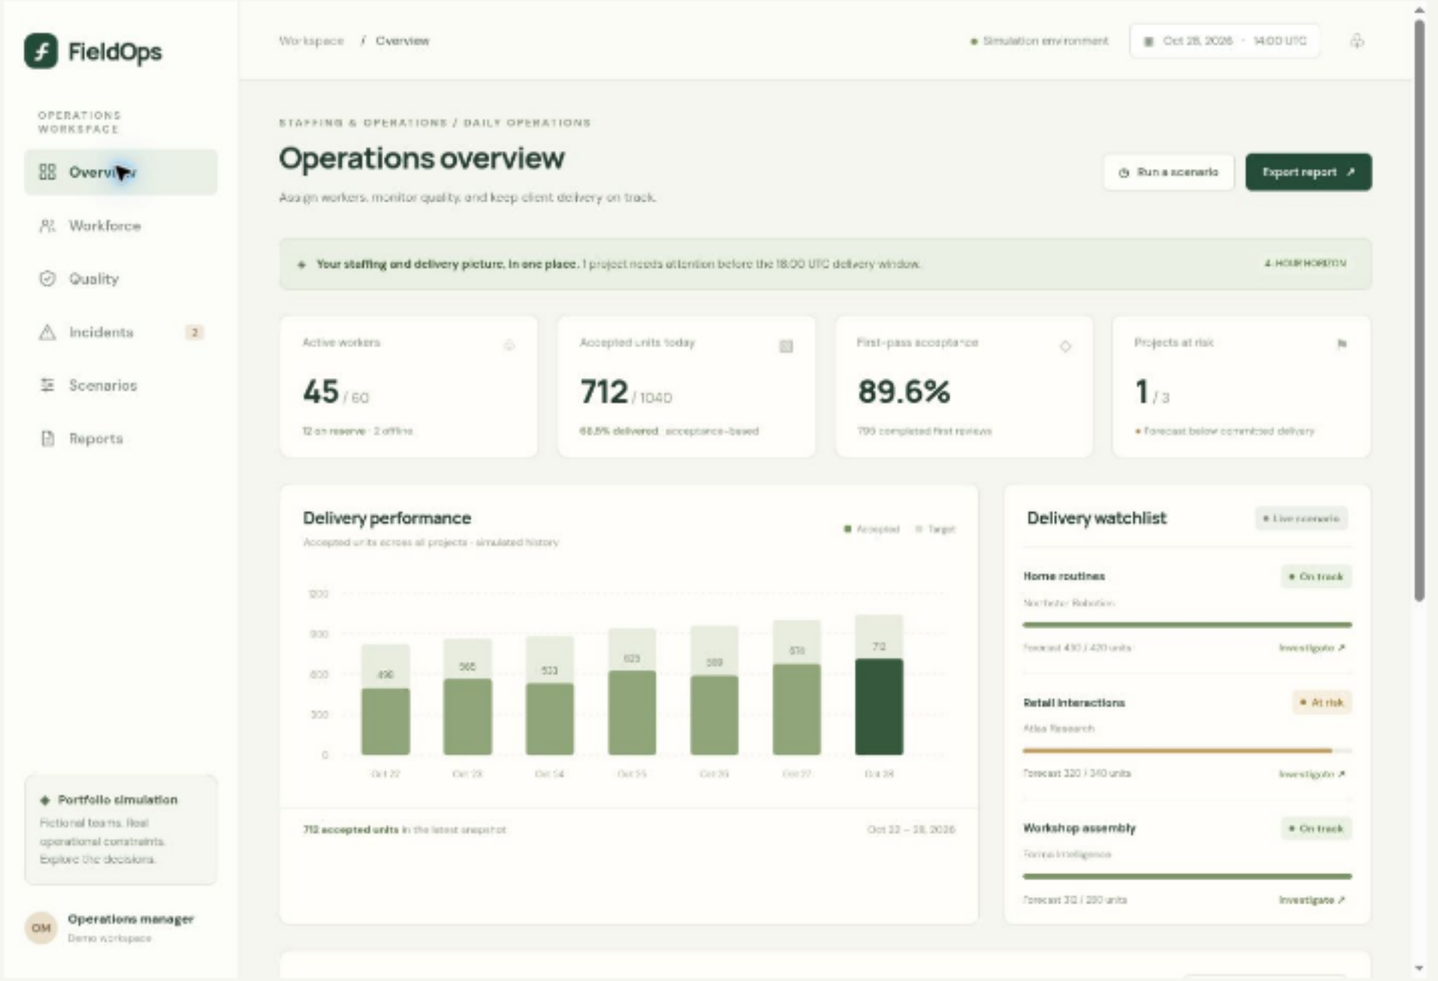


Actual app screen. The baseline includes 45 active workers and 12 available reserves.

Staffing decisions respect eligibility

Managers search by worker or location and review current assignments.

The app checks availability, project qualifications and an existing assignment before allocating reserve staff.

One shared shift window
14:00–18:00 UTC

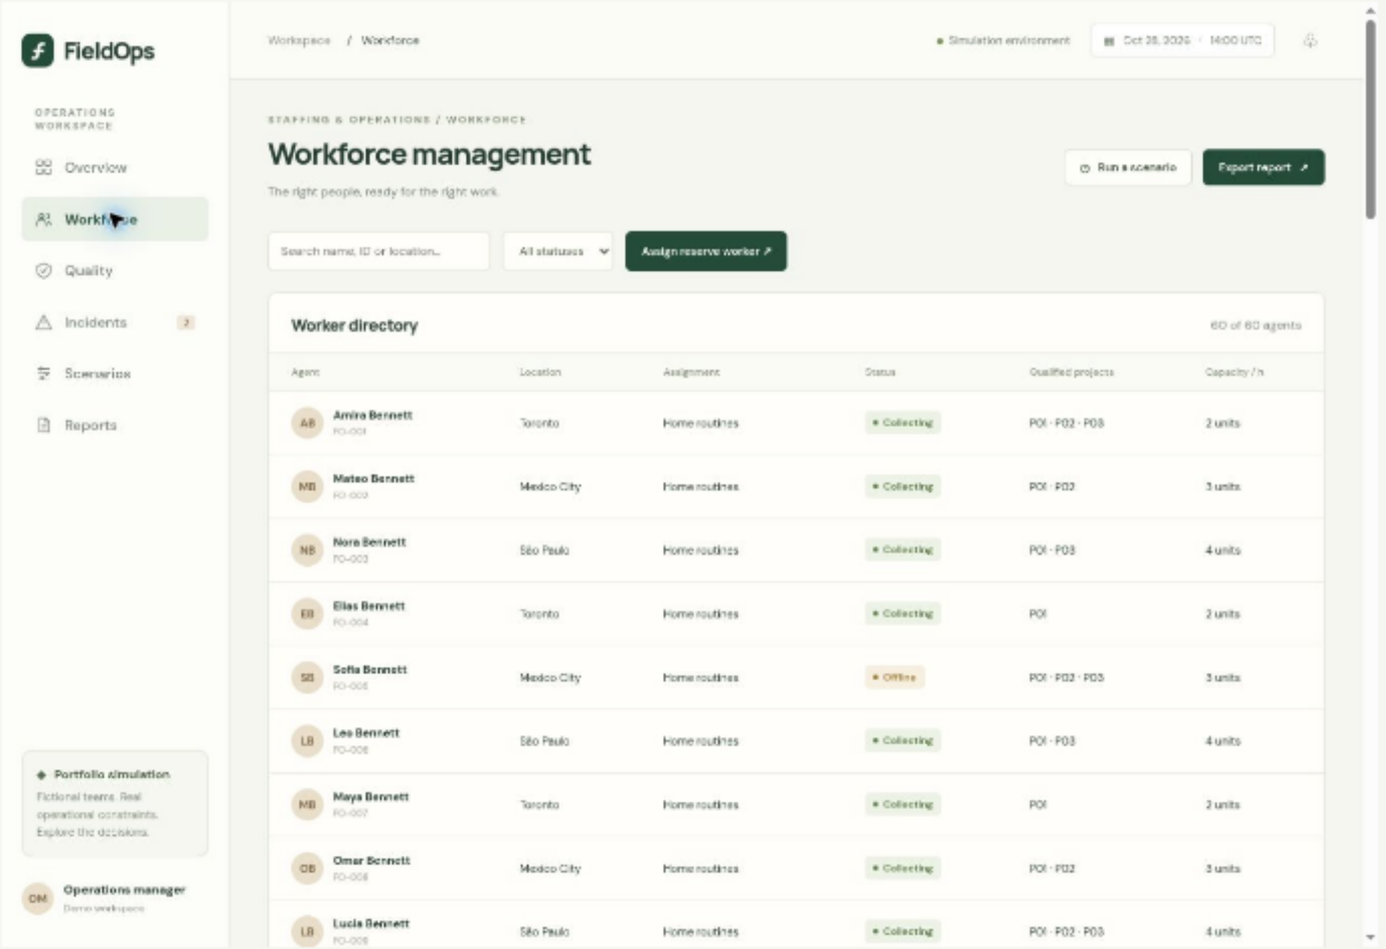


Fictional worker directory. An assigned worker cannot receive a second project in this window.

The investigation explains the bottleneck

Retail interactions projects a shortfall of 20 accepted recordings.

The investigation identifies QA capacity as the constraint and shows qualified reserve workers with their modeled cost.

The manager adds review capacity after assessing the staffing action

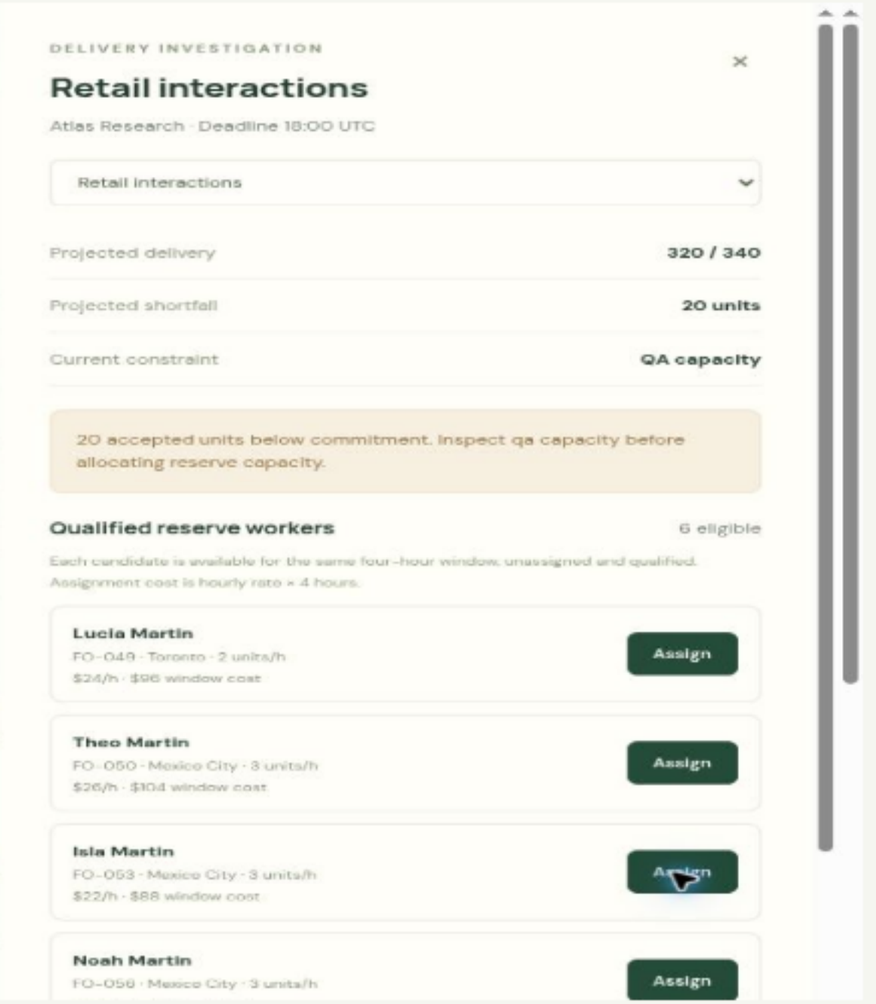

Actual investigation screen before intervention. Historical accepted output remains fixed.

Simulated result of the intervention

Measure	Baseline	After action
Retail projected accepted units	**320**	**341**
Portfolio projected accepted units	**1,062**	**1,083**
Projects below commitment	**1**	**0**
Remaining-window direct cost	**$3,904**	**$4,072**

21 more projected accepted units for $168 in added modeled cost


Simulated forecasts, not achieved client outcomes. Costs exclude existing QA labor and overhead.

The client report follows the scenario

The report explains accepted output, the deadline forecast and each project’s constraint.

Managers can download a CSV or print a summary. The audit records their corrective actions.

Changes persist in the current browser and can be reset

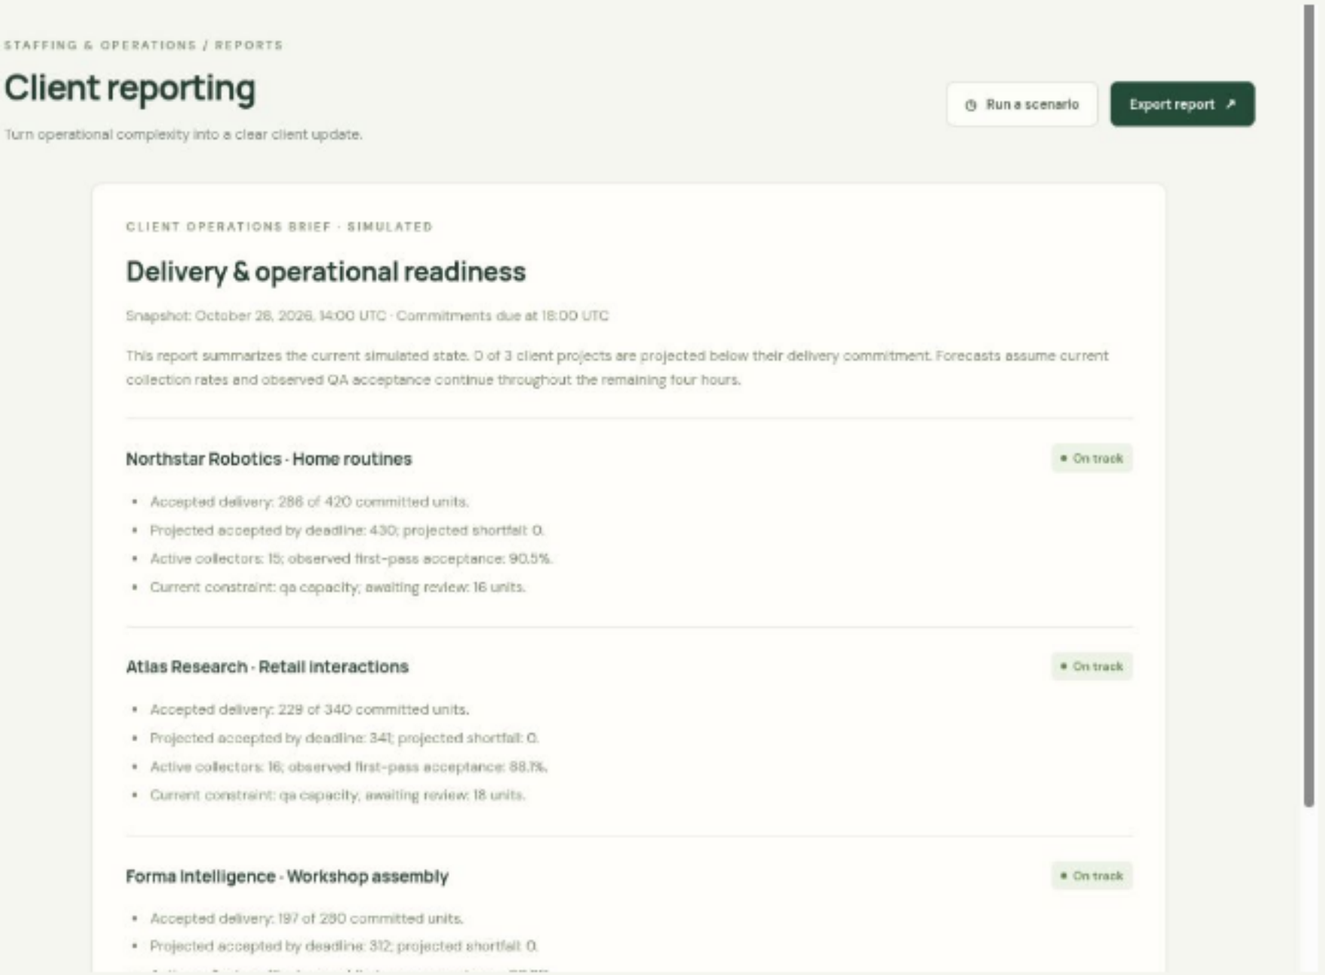

Actual report screen after intervention. All client and operational information is simulated.

Completed portfolio prototype

Delivered

Interactive application
Business case and introduction
Model checks and walkthrough
Screenshots and presentation

Defined scope

Deterministic simulation
Browser-local storage
One shared shift window
No live workforce integrations

github.com/enzosafadi/FieldOps

Public demo source. Hosted app currently requires the owner’s ChatGPT access.
